



Source: FHWA

May 5, 2023

Cape Meares Road Relocation

Construction Activities & Upcoming Work

The project achieved a major milestone this week in the completion of MSE Wall No. 2. In addition, construction began on MSE Wall No. 3 and is expected to continue for the next 4 to 6 weeks. A geotechnical engineer was onsite this week to oversee the beginning phases for MSE Wall No. 3. Truck traffic between the south project entrance and the adjacent Lighthouse Quarry will remain active but at varying levels in the coming weeks.

ROAD CLOSURES

Current road closure points will remain in effect on Bayocean Road near the Cape Meares Lighthouse, and approximately 0.5 miles south of the Lighthouse. Construction will have minimal impact on public traffic as it is closed to through traffic. Please be advised that project limits are outside the gate on Cape Meares Loop coming south from Bayocean Road. See map on the following page for areas not accessible to the public.

Project Website:

<https://highways.dot.gov/federal-lands/projects/or/tillamook-b780-1>



View of completed MSE Wall No. 2.

Source: FHWA

Project Number:
OR TILLAMOOK B780
(1)

FHWA Contact:
John Henderson
john.henderson@dot.gov
360-839-3867

Project Partner:
Tillamook County
Federal Highway
Administration
Western Federal Lands
Highway Division

Contractor:
M.A. DeAtley Construction, Inc.
829 Evans Rd,
Clarkston, WA 99403

Notice to Proceed:
December 6, 2021.

Fixed Completion Date:
October 31, 2023




U.S. Department
of Transportation

**Federal Highway
Administration**

Western Federal Lands Highway Division

OR TILLAMOOK B780(1), Cape Meares Road Relocation

Map

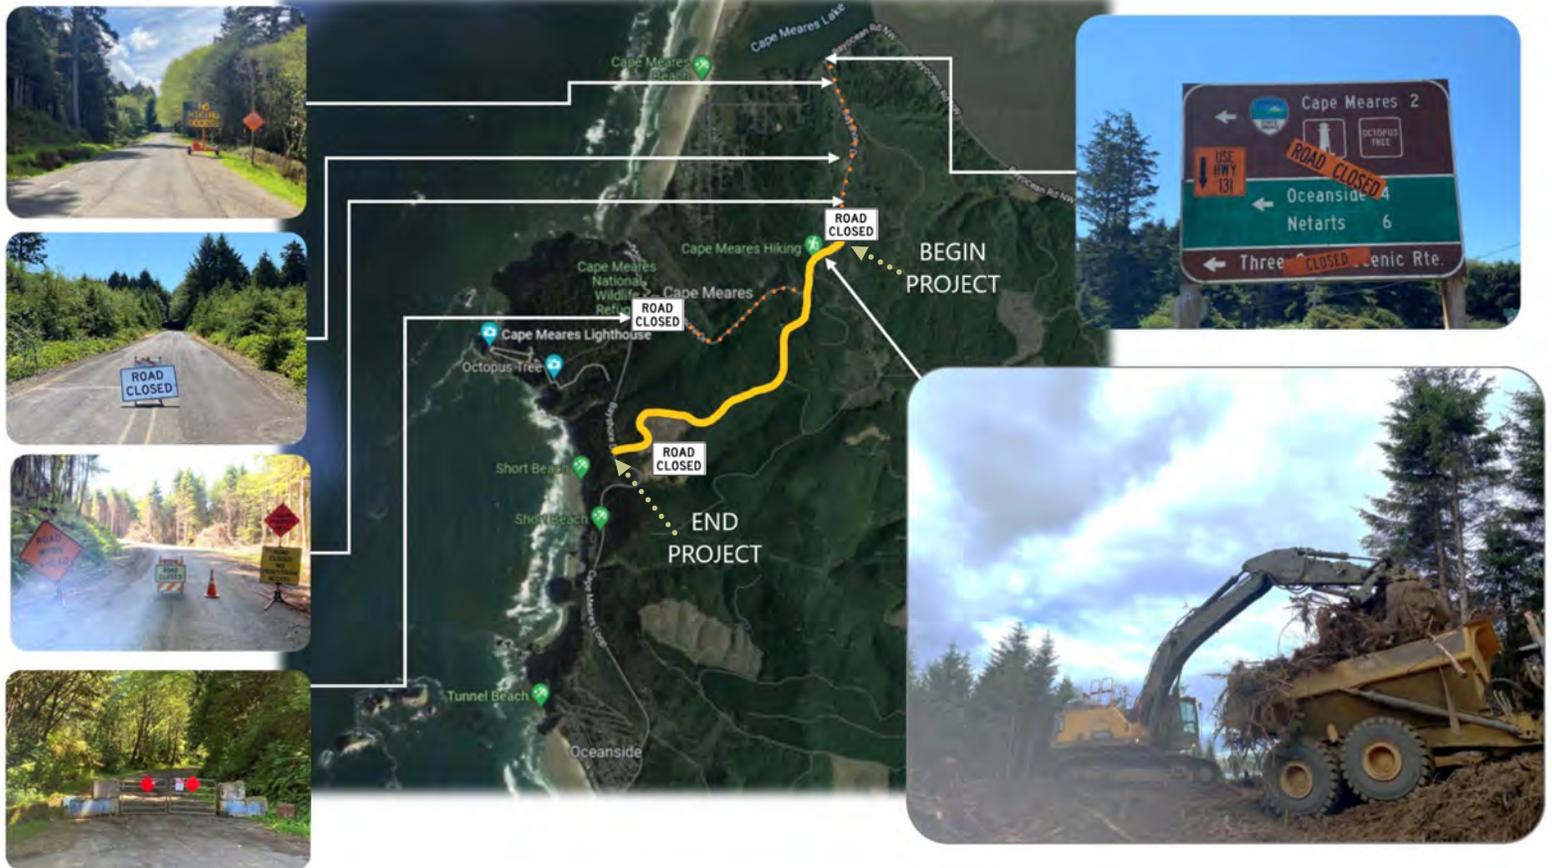

Map Source: Google

All project images
Source: FHWA

Project location and areas closed off to the public.

OR TILLAMOOK B780(1), Cape Meares Road Relocation

Pictures



**View of
Completion of the
first course of MSE
Wall No. 3.**



**View of
construction of the
fourth course at MSE
Wall No.3.**
